

# Pontoon Dock

Issue 20 – April 2019



A development by



Welcome to the April issue of the Pontoon Dock development newsletter, looking at the latest progress achieved and upcoming milestones.

## Significant Events

The electrical substations of the project were connected to the electrical network on 15<sup>th</sup> March 2019. Open Doors visits were hosted on site on 19<sup>th</sup> and 22<sup>nd</sup> March. Façade scaffold dismantling and balconies install will start in April 2019.

## Progress to date – Works completed

**Envelope:** Installation of windows completed. Brickwork façade completed up to level 14 in blocks A & B, up to level 11 in block C.

**Internals:** Apartments fit-out in Blocks A, B & C levels 1 to 14 ongoing. Corridors fit-out started.

**Externals:** Water supply connection completed.

## Forthcoming milestones – Tasks starting in April


**Envelope:** Completion of brickworks on the tower blocks. Start scaffold dismantling and installation of balconies. Completion of roofs waterproofing.

**Internals:** Start energising and testing the apartments. Start final decoration in the apartments.

**Externals:** Start podium waterproofing.

## Caring for the Environment

At Pontoon Dock, we care about our impact on the environment and, specifically, our carbon footprint. We are closely monitoring this through our online tool, SmartWaste, which allows us to track our carbon emissions from the start of the project.

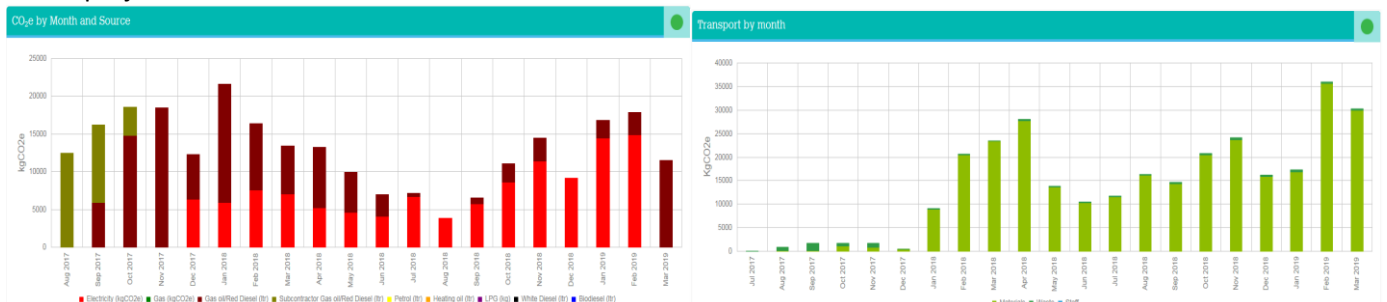

Shared innovation

[www.bouygues-uk.com](http://www.bouygues-uk.com)

# Your safety is our concern

Bouygues UK takes every precaution to keep you safe throughout the construction process.

At all times, our site will be secure and surrounded by fencing but building sites can be hazardous places:

- We dig deep holes
- We erect scaffolding
- We use large, noisy machinery

**Please do not enter the construction site, unless it is part of a pre-arranged visit by our project team.**

- Our operatives and staff are trained to work safely

Please help us to keep you and children safe, and take extra care during the school holidays.



**HEALTH  
& SAFETY  
A SHARED  
COMMITMENT!**

## Considerate Constructors Scheme

Bouygues UK firmly supports the aims of the Considerate Constructors Scheme. All of our sites are registered with the Scheme, and regular visits from the Considerate Constructors monitor will help us to ensure that we continue to improve our performance in showing full respect for:

- Appearance
- Community
- Environment
- Safety
- Workforce

Please let us know if you have any concerns.

Our contact details are on the newsletter that you should regularly receive or on the site hoardings.

If you would like further information regarding the Scheme you can visit their website at [www.ccscheme.org.uk](http://www.ccscheme.org.uk)



### Want to speak to us?

### Standard site working hours are:

Monday to Friday:  
7.30am-6pm

Saturday (if needed):  
8am-1pm

There should be no noisy works before 8am.

For more information about the development, please go to <http://www.pontoondockdevelopment.com/>. In the next few months, we hope to update the website with news of developments in the project. The website also provides details for employment opportunities being created by the project, for those interested.

### Communication and Community Liaison

Bouygues UK is committed to working with the local community and keeping clear and open lines of communication throughout the construction phase. We have appointed **Myra Carino** as our resident liaison officer. Please do write to us should you have any questions or concerns.

### Your contacts



Left: **Ghassan Ali** – Project Manager  
Email: [ghassan.ali@bouygues-uk.com](mailto:ghassan.ali@bouygues-uk.com)

Right: **Myra Carino** – Project Assistant  
Email: [myra.carino@bouygues-uk.com](mailto:myra.carino@bouygues-uk.com)  
Phone: 0800 083 7286



**Shared innovation**

[www.bouygues-uk.com](http://www.bouygues-uk.com)
